



Three-level Centers of Professional Excellence: Qualification, Entrepreneurship and Innovation in the Green Economy

Project Meeting

Szczecin, 23.-24.11.2023



Co-funded by the
Erasmus+ Programme
of the European Union




Agenda



Thursday, 23.11.2023			
Time	What	Moderation	Venue
08:45 – 09:00	Arrival of the partners at Marshall Office		Marshall Office Delfin conference room Marszałka Józefa Piłsudskiego 42, 70-421 Szczecin
09:00 – 09:30	1) Welcome	PP1 HP	
09:30 – 10:00	2) WP1 Management	PP1 HP	
10:00 – 10:30	3) WP2 Overview	PP1 HP	
10:30 – 11:00 Coffee break			
11:00 – 12:00	4) WP2 - Workshop	PP1 HP All	
12:00 – 13:00 Lunch at Marshall Office			
13:00 – 13:45	5) WP3 Overview	PP1 HP	
13:45 – 14:30	6) WP4 Overview	PP1 HP	
14:30 – 15:00 Coffee break			
15:00 – 15:45	7) WP5 Overview	PP1 HP	
15:45 – 16:00	Wrap up day 1	PP1 HP	
16:00 – 16:30	Tour around the Marshall Office		
17:30 – 18:30 City tour on the bus			Meeting point: In front of Radisson Blu Hotel, Szczecin Plac Rodła 10, 70-419 Szczecin
19:00 3LoE project dinner			Ceglana Owocowa 14, 70-213 Szczecin

Friday, 24.11.2023			
Time	What	Moderation	Venue
08:45 – 09:00	Arrival of the partners at the chamber		Izba Rzemieślnicza w Szczecinie al. Wojska Polskiego 78, 70-482 Szczecin
09:00 – 10:30	8) 7min presentation by each CoVE	PP1 HP	
10:30 – 11:00 Coffee break			
10:30 – 11:30	9) Round tables - exchange of experience	PP1 HP	
11:30 – 12:00	10) Wrap-up and evaluation of meeting	PP1 HP	
12:00 - 13:00 Lunch and farewell as well as optional visit to Willa Lentza			



Co-funded by the
Erasmus+ Programme
of the European Union

A vibrant European town square with colorful buildings and bicycles parked in the foreground. The scene is captured during the day with a slightly dimmed, cinematic lighting. In the foreground, several bicycles are parked in a black metal rack on a cobblestone-paved square. The background features a row of multi-story buildings with varied architectural styles and colors. From left to right, there is a yellow building, a white building with pink vertical stripes, a blue and white half-timbered building, a white building with a mansard roof, a white building with a domed roof, and a brick building. A red awning is visible over a cafe area on the left. The sky is a clear, pale blue.

TOP1 Welcome



TOP1 Welcome



Aim of the meeting:

1. To clarify organisational questions
2. To understand the status of the activities and CoVEs
→ Last official project meeting before final project meeting and conference in September 2024
3. To have a good time :)



Co-funded by the
Erasmus+ Programme
of the European Union



**TOP2
WP1 Management**



TOP2 Interim report C



Reporting period: 01.11.22 - 31.10.23

- Keep the reporting deadline **30.11.23** and send all documents at once to: mhenke@hanse-parlament.eu
- The reporting includes three parts:

1) The narrative reporting.

→ A **concise and concrete** summary of activities of max. 2 pages. See: **Template “3LoE_Interim report C_narrative part_template”**.

2) The financial reporting (Staff costs, travel costs, other costs, subcontracts)

→ All partners have to **submit an overview of all costs for the entire project period 01.11.2020 - 31.10.2023**. See: **Template “Overview of all costs for reporting period”**.

All templates and supporting information for the reporting can be found in the GDrive:

<https://drive.google.com/drive/folders/1ktAdjV5XUD9tLMfhXuJeCdrZZxJ2qLUD?usp=sharing>

3) The dissemination reporting.

→ All partners are asked to update all dissemination activities from **01.11.2020 to 31.10.2023** in the excel file created by PP13 IAGF by 30.11.2023 and upload it directly in the GDrive:

https://drive.google.com/drive/folders/11fOZVRQsAeinBVDqhjSfvvlhLWJcg-eC?usp=share_link. See: **Template “Template_Documentation_Dissemination”**.

Please note: We can only give advice but responsibility of reporting lies with each individual partner (more than 200 people working on 3LoE project)





TOP2 Feedback Interim Report B



Key remarks by the EACEA:

- *“The consortium is recommended to report about the main **results of evaluations** of training programmes and to elaborate how the results of evaluations of numerous training programmes were integrated in the potential **revisions of the educational programmes.**”*
- *“Due to the fact that CoVEs operate as a three level tier, there are strong cooperations between educational institutions on initial vocational level, further vocational level and at higher education level. The project is recommended to support the evidence on these strong relationships with an **overview of quantitative details** regarding the level of involvement **of different stakeholders** in each CoVE.”*
- *“The project is recommended to provide a more detailed overview of **quantitative achievements related to dissemination** activities.”*





TOP2 Budget



➤ The pre-payments have been adjusted according to budget change.

Partners who can request a pre-payment via informal e-mail:

- PP2 HWKD (3rd)
 - PP4 CHSZ (3rd after proof of 70% spent)
 - PP7 VESK (3rd)
 - PP14 WIFI (3rd)
 - PP15 HS02 (3rd)
 - PP17 SFC (2nd & 3rd)
 - PP20 IPM (3rd)
 - PP21 ES (3rd after proof of 70% spent)
 - PP22 VISC (1st, 2nd, 3rd)
 - PP24 BHH
 - PP25 AGBAR
-
- Budget changes still possible, up to 10% no need for EU amendment
 - Partners receiving more than €300,000 of EU funding need to subcontract an official auditor for the final financial report





TOP2 Next meetings



Next CoVE Forum

10-12 September 2024 Lyon (<https://www.copcov.es/forum-2023/>)

Project Meeting and Conference in Riga, September 2024 (organised by PP11 RSU)

→ **Original dates (12th & 13th of September 2024) need to be changed**

New suggested dates:

3rd of September: Arrival

4th of September: Project meeting and Hanse Parliament general assembly

5th of September: 3LoE conference

6th of September: Departure

What do you think?

Online Meeting:

➤ February 20th 2024 09:00-12:00 on Zoom

➤ **Bilateral (online) meetings in between**



Co-funded by the
Erasmus+ Programme
of the European Union



Questions regarding
WP1 Management?



TOP3

WP2 Development and permanent operation of regional centers of excellence and transnational platform



Co-funded by the Erasmus+ Programme of the European Union



WP2 Results Overview



<u>Results</u>	<u>Status</u>	<u>Deadline</u>	<u>Comments</u>
2.1 Analyses and recommendations	Done		
2.2 Three-level centres of professional excellence "Green Economy for SMEs" and transnational platform	Ongoing	31.10.24	This deliverable is comprised of three parts: A Concept (done) B Tool and extension (done) C Evaluation and Continuation (by 31.10.24)
2.3 Training programs for personnel and center management	Done		
2.4 Political strategy and action program	Ongoing	31.07.24	WP2 A11 Analysis of all EU funding opportunities & WP2 A12 Development, consulting and introduction of political strategy program by PP22 VISC





WP2 Result 2.4 Political strategy and action program by PP22 VISC



- **WP2 A12 Political strategy and action program by PP22 VISC**
 - a) PP22 VISC asked all project partners to send short country reports by 31.10.2023.
 - b) PP22 VISC preparation of a first draft by 31.10.2023.
 - c) Consultation in Szczecin.
 - d) Examination and incorporation of the proposals of the partners and the results of the workshop by 31.01.2024.
 - e) Consultation and coordination with PP1 HP and PP13 IAGF by 28.02.2024.
 - f) Sending of the strategy program to all partners with the request for written comments by 31.03.2024.
- **WP12 A11 Analysis of all EU funding opportunities by PP22 VISC**
 - a) First draft 31.10.2023.
 - b) Finalization 31.03.2024.

→ **Short update by PP22 VISC**





WP2 A13 Evaluation of the CoVEs (Part of Result 2.2)



- **WP2 A13 Evaluation of the construction and operation of the CoVEs:**
 - a) Part I: 1st online questionnaire *"3LoE Evaluation on the "Construction, operation and cooperation of the Center of vocational Excellence (CoVE)" - Survey for Project Partners"* to be filled out by all partners (20 responses by December 2021)
 - b) Part II: 2nd online questionnaire *"3LoE Evaluation on the "Construction, operation and cooperation of the Center of vocational Excellence (CoVE)" - Second Survey"* to be filled out by all partners (22 responses by November 2023)
 - c) Personal interviews during the first half of 2024 with:
 - the coordinator of every CoVE
 - all other CoVE partners,
 - other participating VET/higher education institutions and,
 - if possible, with local/regional education authorities
-
- PP1 HP interviewing CoVEs Germany, Poland and Spain
 - PP13 IAGF interviewing CoVEs Austria and Italy -
 - PP22 VISC interviewing CoVEs Lithuania and Latvia

→ PP1 HP, PP13 IAGF, PP22 VISC will be in touch with every partner



Co-funded by the
Erasmus+ Programme
of the European Union




WP2 A13 Evaluation of the CoVEs (Part of Result 2.2)



Part I: 1st online questionnaire “3LoE Evaluation on the “Construction, operation and cooperation of the Center of vocational Excellence (CoVE)” - Survey for Project Partners” to be filled out by all partners (20 responses by December 2021)

Please indicate your country

Answered: 20 Skipped: 1

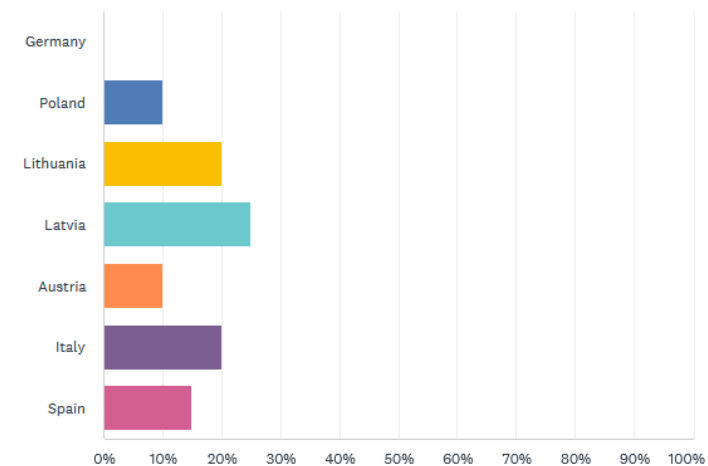

ANSWER CHOICES	RESPONSES
Germany	0.00% 0
Poland	10.00% 2
Lithuania	20.00% 4
Latvia	25.00% 5
Austria	10.00% 2
Italy	20.00% 4
Spain	15.00% 3
TOTAL	20




Co-funded by the Erasmus+ Programme of the European Union



WP2 A13 Evaluation of the CoVEs (Part of Result 2.2)



Part II: 2nd online questionnaire “3LoE Evaluation on the “Construction, operation and cooperation of the Center of vocational Excellence (CoVE)” - Second Survey” to be filled out by all partners (22 responses by November 2023)

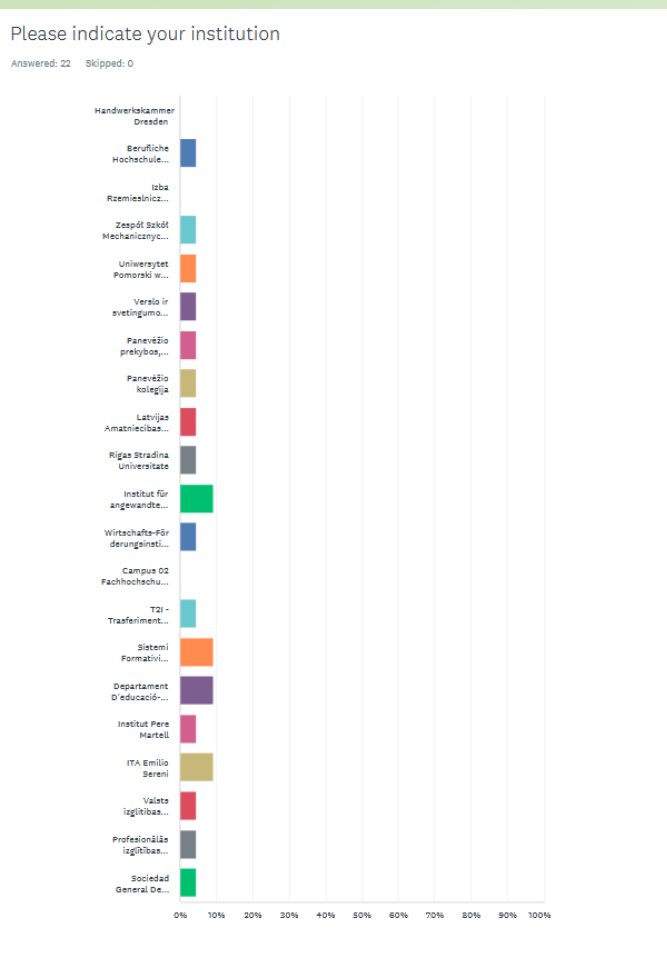

ANSWER CHOICES	RESPONSES
Handwerkskammer Dresden	0.00% 0
Berufliche Hochschule Hamburg	4.55% 1
Izba Rzemielnicza Malej i Sredniej Przedsiębiorczosci	0.00% 0
Zespół Szkół Mechanicznych i Logistycznych w Stupsku	4.55% 1
Uniwersytet Pomorski w Stupsku	4.55% 1
Verslo ir svetīgumo profesionālās karjeras centras	4.55% 1
Panevėžio prekybos, pramonės ir amatų rūmai	4.55% 1
Panevėžio kolegija	4.55% 1
Latvijas Amatniecības kamera	4.55% 1
Rīgas Stradiņa Universitāte	4.55% 1
Institut für angewandte Gewerbeforschung der Wirtschaftskammer Österreich	9.09% 2
Wirtschafts-Förderungsinstitut der Wirtschaftskammer Steiermark	4.55% 1
Campus 02 Fachhochschule der Wirtschaft	0.00% 0
T2I - Trasferimento Tecnologico e Innovazione	4.55% 1
Sistemi Formativi Confindustria	9.09% 2
Departament D'educació- Generalitat de Catalunya	9.09% 2
Institut Pere Martell	4.55% 1
ITA Emilio Sereni	9.09% 2
Valsts izglītības saturs centrs	4.55% 1
Profesionālās izglītības kompetences centrs Liepājas Valsts tehnikums	4.55% 1
Sociedad General De Aguas De Barcelona	4.55% 1
TOTAL	22



Co-funded by the Erasmus+ Programme of the European Union



WP2 CoVE Result template



- WP2 A2.2, WP2 A2.2.1, WP2 A2.3, WP2 A2.4, WP2 A2.5, WP2 A2.6, WP2 A1.7, WP2 A2.8, WP2 A3.1, WP2 A3.2, WP2 A6, WP2 A7, WP2 A8, WP2 A9, WP2 A10 will be summarised in **one report per CoVE (deadline 31.10.2024)**.
- PP1 HP has developed a template for such a report with the following contents:
- We will do a workshop on this now.





WP2 CoVE Result template - Workshop



- 60min.



Co-funded by the
Erasmus+ Programme
of the European Union



Questions regarding
**WP2 Development and permanent
operation of CoVEs?**



TOP4

**WP3 First center
level "Vocational
training"**



WP3 Results Overview



<u>Results</u>	<u>Status</u>	<u>Deadline</u>	<u>Comments</u>
3.1 Tool for vocational guidance and training for teachers	Almost done		PP4 CHSZ implementation report missing
3.2 Training program for teachers to conduct DVT	Done		
3.3 Four Curricula for specific dual vocational training	Ongoing	30.06.2024	This deliverable is comprised of five parts: A Preparation and transfer of the German dual vocational training systems in English and German (done) B Curricula in English and German (done) C Implementation reports (testings ongoing, reports by 30.06.24) C Evaluation concept (done) D Evaluation reports (to be written after evaluations of testings by 30.06.24)
3.4 Dual vocational training for people with special learning needs	Ongoing	30.06.2024	This deliverable is comprised of four parts: A Concept and two curricula (done) B Implementation report (testing started in September 2022, report by 30.06.24) C Evaluation concept (done) D Evaluation report (to be written after the testing) E Strategy program (in progress)





WP3 Results Overview



Results	Status	Deadline	Comments
3.5 Six Training programs for strong learners in initial vocational training	Ongoing	30.06.2024	This deliverable is comprised of the following parts: A: Curriculum A (done) B: Implementation reports of Curriculum A tests (by 30.06.24 after testing) C: Curriculum B (done) D: Implementation reports of Curriculum B tests (by 30.06.24 after testing) E: Curriculum C (done) F: Implementation reports of Curriculum C tests (by 30.06.24 after testing) G: Curriculum D (done) H: Implementation reports of Curriculum D tests (by 30.06.24 after testing) I: Curriculum E (done) J: Implementation reports of Curriculum E tests (by 30.06.24 after testing) K: Curriculum F (done) L: Implementation reports of Curriculum F tests (by 30.06.24 after testing) M: Evaluation concept (done) N: Evaluation report (by 30.06.24 after testing)
3.6 Training programmes for the training of trainers in SMEs	Ongoing	<u>31.10.23</u>	This deliverable is comprised of four parts: A Curricula (done) B Implementation reports (by 31.10.23 after testing) C Evaluation concept (done) D Evaluation report (by 31.10.23 after testing)
3.7 Two-year Training "Sustainable restaurant worker"	Ongoing	30.06.2024	This deliverable is comprised of two parts: A Curriculum (done) B Implementation report (by 30.06.24 after testing)
3.8 Five-year technician training „Ecologic Solutions in Logistics“	Ongoing	30.06.2024	This deliverable is comprised of four parts: A Curriculum (done) B Implementation report (by 30.06.24 after testing) C Evaluation concept (done) D Evaluation report (by 30.06.24 after testing)
3.9 Business Ideas Pupils in Green Economy	Done		





WP3 A1 Tool for vocational and qualification counselling



WP & Activity	Partner	Target group	No. of participants	Timeline	Implementation report	Evaluation data	Evaluation report	Comments
WP3 A1.2 Tool for vocational and qualification counselling	PP2 HWKD	Pupils secondary level	7	January 2022	done	7 responses	done By PP3 BAHH	Ready as Result 3.1 Tool for vocational and educational guidance and training for teachers and consultants
	PP4 CHSZ	???	15	???	Implementation report missing	???		
	PP7 VESK	VET students age 17-19	15	October – November 2021	done	15 responses		
	PP10 LAK	Generation Z students	15	October – November 2021	done	14 responses		
	PP14 WIFI	Trainees age 17-26	8	October – December 2021	done	7 responses		
	PP17 SFC & PP21 ES	VET students age 19-26	28	December 2021	done	28 responses		
	PP20 IPM & PP18 DEGC	VET second-year students	14	November 2021 – January 2022	done	14 responses		
Sum:			102			85		





WP3 A4 Implementation of dual vocational trainings



WP & Activity	Partner	Target group	No. of participants	Timeline	Implementation report	Evaluation data	Evaluation report	Comments
WP3 A4.3 Dual vocational trainings	PP4 CHSZ "Electrician" and „Fitter of fixtures and fittings in building industry"	VET students	15	Started September 2022 Finalisation after project end	in progress	15+15 (to be answered by PP6 APS) second survey in Spring 2024	Evaluation report by 31.07.24 by PP6 APS	Result 3.3 Four Curricula for specific dual vocational training
	PP7 VESK "Cook"	VET students	15	Started September 2021	in progress	15 (to be answered by PP6 APS) second survey in Spring 2024		
	PP23 LVT "Motor vehicle mechanic/Car mechanic"	VET students	22	Started September 2022 Finalisation May 2024	in progress	21 (to be answered by PP6 APS) second survey in Spring 2024		
	PP20 IPM "Electromechanic"	VET students	42	Started September 2021 January 2023 new program started (fusion of 2 curricula) Finalization May 2024	in progress (preparation end of February / activity start March 2023)	18 (to be answered by PP6 APS) second survey in Spring 2024		
Sum:			94			83		





WP3 A5 Training for trainers in SMEs



WP & Activity	Partner	Target group	No. of participants	Timeline	Implementation report	Evaluation data	Evaluation report	Comments
WP3 A5 Training for trainers in SMEs	PP2 HWKD	SME workers	14	10-27th January 2022	done	12 questionnaire responses	done By PP1 HP	Result 3.6 Training programs for the training of trainers in SMEs
	PP4 CHSZ	SME workers	11	20.08 - 04.09 2021	done	0 questionnaire responses		
	PP5 ZSML	Employees	19	May – October 2022	done	0 questionnaire responses		
	PP8 PCCIC	In-company trainers	19	October 2021 – January 2022	done	18 questionnaire responses		
	PP10 LAK	Individual merchants, SMEs	15	April 2022 – June 2022	done	15 participants, 1 trainer		
	PP23 LVT	SME workers	9	October 2021 – January 2022	done	5 questionnaire responses		
	PP14 WIFI	Employees, SME workers, CEOs, Craftmanship	face-to-face 261, online 42	2022	done	103 online feedbacks		
	PP17 SFC	Employees	5	March - September 2023	done	27 participants, 1 trainer		
	PP20 IPM	Employees	14	November 2021 - January 2022	done	12 questionnaire responses		
Sum:			367 (+42 online)			194		





WP3 A6.2 Test Specialist for Building Insulation by PP23 LVT



WP & Activity	Partner	Target group	No. of participants	Timeline	Implementation report	Evaluation data	Evaluation report	Comments
WP3 A6.2 Tests "Specialist for Building Insulation"	PP23 LVT	VET students	16	Started September 2022	pending	"Surveys have not yet been answered" - PP9 PC	pending	Result 3.4 Dual vocational training for people with special learning needs
Sum:			16					





WP3 A7 Additional qualification trainings



WP & Activity	Partner	Target group	No. of participants	Timeline	Implementation report	Evaluation data	Evaluation report	Comments
WP3 A7.21 A Technologies water supply	PP18 DEGC (Institut Esteve Terradas)	HE students	26	September 2022 – January 2023	done	26 questionnaire responses	Pending by PP9 latest by 30.06.2024?	Result 3.5 Six Training programs for strong learners in initial vocational training
	PP25 AGBAR	?	?	?	? Latest by 30.06.2024?	?		
WP3 A7.22 B Technologies water saving	PP4 CHSZ	students, SME workers	12	December 2022 - finished October 2023	Pending By 30.11.2023?	“Surveys have not yet been answered” - PP9 PC		
	PP20 IPM	students	pending - difficult to find students that have enough time	pending	Pending Latest by 30.06.2024?	pending		
	PP25 AGBAR	?	?	?	? Latest by 30.06.2024?	?		
WP3 A7.23 C Greywater and rainwater utilization technologies	No implementation							
WP3 A7.24 D Technologies decentralized wastewater treatment	No implementation							
Sum:			38			26		





WP3 A7 Additional qualification trainings



WP & Activity	Partner	Target group	No. of participants	Timeline	Implementation report	Evaluation data	Evaluation report	Comments
WP3 A7.25 E Fundamentals of the circular economy	PP5 ZSML	Vet students (students from Ecologistics 2,5 class)	78	September 2022 – April 2023	pending By 30.11.2023?	?	Pending by PP9 latest by 30.06.2024?	Result 3.5 Six Training programs for strong learners in initial vocational training
	PP7 VESK	Vet students	25	November 2022 – April 2023	pending By 30.11.2023?	? See coment		
	PP8 PCCIC	Vet students	pending	Starting September 2023	pending	pending		
	PP9 PC	Students	11	September 2021 – December 2021	done	11 responses		
	PP10 LAK	Individual craftsmen, SME workers	15	September 2023 - October 2023	implementation report by 13.11.2023	? 30.11.2023		
	PP16 T2I	Vet students	20	October 2022 – April 2023	done	?		
WP3 A7.26 F Systemic solution-oriented consulting	PP10 LAK	Individual craftsmen, SME workers	?	May 2023 - June 2023	implementation report by 13.11.2023	? 30.11.2023		
Sum:			149			11		





WP3



WP & Activity	Partner	Target group	No. of participants	Timeline	Implementation report	Evaluation data	Evaluation report	Comments
WP3 A7.27 Customer service fitter modules for initial training	PP2 HWKD with BSZ Zeuner	?	?	pending	Implementations report by 31.03.24	pending	Own evaluation?	Result 3.5 Six Training programs for strong learners in initial vocational training
WP3 A8 Sustainable restaurant worker	PP7 VESK	Vet students	15	in progress	pending	pending	Own evaluation?	Result 3.7 Two-year Training "Sustainable restaurant worker"
WP3 A9.1 Technician training „Ecologic Solutions in Logistics“	PP5 ZSLM	Vet students	77	in progress	pending	30 responses	in progress By PP6 APS	Result 3.8 Five-year technician training „Ecologic Solutions in Logistics“
WP3 A10 Latuaideadimpresa	PP17 SFC	Vet students age 16-18	2125	done	done	No evaluation		Result 3.9 Business Ideas Pupils in Green Economy
Sum:			2217			30		





Questions regarding
WP3 First center level "Vocational
training"?



TOP5

WP4 Second center
level "Continuing
vocational training"



WP4 Results Overview



<u>Results</u>	<u>Status</u>	<u>Deadline</u>	<u>Comments</u>
4.1 Concepts and Instruments for Management and implementation qualifications	Done		
4.2 KAIN Method and Train the Trainer Program	Done		
4.3 Six Green Economy training programs	Ongoing	30.04.23	This deliverable is comprised of the following parts: A: Curriculum A (done) B: Implementation reports of Curriculum A tests by 30.04.23 C: Curriculum B (done) D: Implementation reports of Curriculum B tests by 30.04.23 E: Curriculum C (done) F: Implementation reports of Curriculum C tests by 30.04.23 G: Curriculum D (done) H: Implementation reports of Curriculum D tests by 30.04.23 I: Curriculum E (done) J: Implementation reports of Curriculum E tests by 30.04.23 K: Curriculum F (done) L: Implementation reports of Curriculum F tests by 30.04.23 M: Evaluation concept (done) N: Evaluation report by 30.04.23
4.4 Training Energy Service Manager	Ongoing	31.06.23	This deliverable is comprised of four parts: A Concept and curriculum (draft done) B Implementation report by 31.06.23 C Evaluation concept by 31.06.23 D Evaluation report by 31.06.23
4.5 Training Enterprise and Entrepreneurship in Green Economy	Ongoing	31.05.23	This deliverable is comprised of the following parts: A Concept and curriculum (draft done) B Implementation report by 31.05.23 after testing C Evaluation concept (draft done) D Evaluation report by 31.05.23 after testing





WP4 Results Overview



<u>Results</u>	<u>Status</u>	<u>Deadline</u>	<u>Comments</u>
4.6 Two Trainings Vocational Master & two Trainings Technician	Ongoing	30.06.24	
4.7 Integration programme for the unemployed	Almost done	31.04.23	
4.8 Concept "SME-fair digitalization" & 2 Trainings teacher digital Skills	Almost done	30.04.23	
4.9 Five Trainings Energy Saving and Renewable Energies	Ongoing	30.04.23	
4.10 Four specific trainings in the Green Economy	Ongoing	30.06.24	
4.11 Regulations for new continuing education occupational profiles	Ongoing	31.07.24	





WP4 A5 Trainings Energy Saving and Renewable Energies



WP & Activity	Partner	Target group	No. of participants	Timeline	Implementation report	Evaluation data	Evaluation report	Comments
WP4 A5.1 Training I for SMEs: Energy Efficiency and Renewable Energies	PP8 PCCIC & PP9 PC	Business owners, managers, employees	19	April - May 2022	done	No evaluation	No evaluation	Result 4.9 Trainings Energy Saving and Renewable Energies.
	PP10 LAK	Individual craftsmen, SME workers	15	October 2022	Implementation report by end of November			
	PP16 T2I with Padua University	Business owners, managers, employees	35	Nov - Dec 2022	done			
WP4 A5.2 Training II for SMEs: Solar Energy – Technology and Applications	PP10 LAK	Individual craftsmen, SME workers	15	December 2022	Implementation report by end of November			
	PP20 IPM	HE students	20	4th-18th May	done			
WP4 A5.3 Training III for SMEs: Energy Efficient Construction and Application of Renewable Energies	PP10 LAK	Individual craftsmen, SME workers	15	November 2022	Implementation report by end of November			
WP4 A5.4 Training IV for SMEs: Waste and Wastewater Management and Energy Production	PP25 AGBAR	SME technicians and managers	Spring 2023	Start in spring 2023.	Pending, discussed with Agbar			
WP4 A5.5 Energy Modular building owner training	PP2 HWKD	?	?	?	Pending latest by 30.06.24	Own evaluation		
WP4 A5.6 Organization and preparation of a "Course of rational media and energy consumption and their production and distribution"	PP4 CHSZ	?	12	?	Pending latest by 30.06.24			
Sum:			131					



WP4 A6 Green Economy Trainings



WP & Activity	Partner	Target group	No. of participants	Timeline	Implementation report / COMMENTS	Evaluation data	Evaluation report	Comments
WP4 A6.2 A Preparation and management of SMEs for work in the Green Economy	PP2 HWKD as "Environmental Representative SME"	?	?	?		Discussed bilaterally	By PP11 RSU Latest by 30.06.24	Result 4.9 Trainings Energy Saving and Renewable Energies.
	PP5 ZSML	SME workers Company representatives	?	start October/November 2023	training started, Mateusz will send an update, goal is to finalize latest end of June 2024	no evaluation data yet	All partners reminded about this	
	PP7 VESK	SME workers	14	May – June 2022	done	no evaluation data yet	Renata reported that the links dont work	
	PP8 PCCIC	Company representatives	15	April – June 2021	done	8 participants, 0 lecturers	(students part) and she reieved no response.	
	PP10 LAK	Individual craftsmen, SME workers	17	September - December 2022	Implementation report by 30.11	no evaluation data yet	Melanie will follow uo with Liga.	
	PP16 T2I with Padua University	?	?	February - May 2024	pending	pending		
	PP17 SFC with ECOLE Assolombarda	SMEs workers	15 (6 companies)	3rd October 2022 – 17th July 2023	done	5 participants, 1 trainer		
	PP18 DEGC	HE students	26	September - November 2022	done	2 lecturers, 12 participants		
Sum:			87			28		





WP4 A6 Green Economy Trainings



WP & Activity	Partner	Target group	No. of participants	Timeline	Implementation report	Evaluation data	Evaluation report	Comments
WP4 A6.2 B Waste reduction and recycling management	PP8 PCCIC	Company representatives	17	October 2021 – January 2022	done	15 participants, 2 teachers	By PP11 RSU Latest by 30.06.24 Partners need to send evaluation data	Result 4.9 Trainings Energy Saving and Renewable Energies.
	PP10 LAK	Individual craftsmen, SME workers	15	September - December 2023	in progress	by 22.12.2023		
	PP18 DEGC	HE students	26	September - November 2022	done	no evaluation data yet		
WP4 A6.2 C Wastewater treatment and recycling management	PP8 PCCIC	Company representatives	17	November 2021 – February 2022	done	no evaluation data yet		
	PP20 IPM	SME workers	?	started October 2023	by 31.01.24	no evaluation data yet		
	PP25 AGBAR	?	?	?	? In progress with PP20	pending		
WP4 A6.2 D Water supply and saving	PP4 CHSZ	students, SMA workers	15	in progress	?	?		
	PP25 AGBAR	SME technicians and managers	?	Spring 2023	By 30.06.2024	pending		
Sum:			90			17		





WP4 A6 Green Economy Trainings



WP & Activity	Partner	Target group	No. of participants	Timeline	Implementation report	Evaluation data	Evaluation report	Comments
WP4 A6.2 E Cradle to Cradle in SMEs	PP2 HWKD	?	?	Implementation planned for 2023	pending	?	By PP11 RSU Latest by 30.06.24	Result 4.9 Trainings Energy Saving and Renewable Energies.
	PP10 LAK	Individual craftsmen, SME workers	17	September 2022 - December 2022	by November 6th 2023	?		
	PP16 T2I	Business owners, managers, employees	6	Implementation planned for Jan - April 2023	done	3 participants (will be completed until November 9th 2023)		
	PP17 SFC: not enough participants (instead: lean management in the building sector?)	pending	pending	pending	pending	pending		
	PP20 IPM with Tarragona Chamber of Commerce	SME technicians and managers	difficult to find participants	Spring 2023	Pending end of June 2024 finalization to keep in mind	pending		
WP4 A6.2 F Energy generation from wastewater and waste	PP25 AGBAR	SME technicians and managers	?	Spring 2023	?	pending		
Sum:			23			3		





WP4 A7 Enterprise and Entrepreneurship in Green Economy



WP & Activity	Partner	Target group	No. of participants	Timeline	Implementation report	Evaluation data	Evaluation report	Comments
WP4 A7.2 Training Enterprise and Entrepreneurship in Green Economy	PP7 VESK	?	22	November 2022 – May 2023	in progress By 31.01.2023	2 lecturers 22 participants	By PP11 RSU Latest by 29.02.2024	Result 4.5 Training Enterprise and Entrepreneurship in Green Economy
	PP8 PCCIC & PP9 PC	?	?	Started October 2022	done	2 lecturers 15 participants		
	PP10 LAK	Individual craftsmen, SME workers	?	May 2023 - June 2023	by 13.11.2023 By 30.11.2023 but overall goal is to finalize beginning of 2024	no evaluation data yet		
	PP16 T2I	entrepreneurs	21	Starting April 2023	done	6 lecturers 21 participants		
	PP17 SFC	aspiring entrepreneurs	12	March - May 2023	done	“questionnaires completed”		
Sum:								





WP4 A8 Energy Service Manager



WP & Activity	Partner	Target group	No. of participants	Timeline	Implementation report	Evaluation data	Evaluation report	Comments
WP4 A8.2 Training Energy Service Manager	PP2 HWKD	Master craftsman	pending	Starting March 2023	pending	no evaluation data yet	By PP11 RSU Latest by 30.06.24	Result 4.4 Energy Service Manager
	PP8 PCCIC & PP9 PC	?	?	Started November 2022	in progress	2 lecturers 13 participants		
	PP16 T2I	technicians, employees, owners	?	October 2023 – March 2024	in progress Finish latest untiol june 2024	no evaluation data yet		
	PP25 AGBAR??	?	?	?	? Will check and report and was not discussed	no evaluation data yet		
	PP23 LVT	pending	pending	Testing planned for 2023	pending No update, in progress, comment from audience was that this was finished and report was sent – Melanie will double check	no evaluation data yet		
Sum:								





WP4 A10 Vocational Master



WP & Activity	Partner	Target group	No. of participants	Timeline	Implementation report	Evaluation data	Evaluation report	Comments
WP4 A10.2 Vocational Master	PP2 HWKD Electric	?	?	Started May 2022	in progress	1 lecturer 11 participants	By PP11 RSU Latest by 30.06.24	Result 4.6 Two trainings Vocational Master
	PP10 LAK Carpenter	Individual craftsmen, SME workers	15	October 2022 - December 2023	in progress Will finish December,	no evaluation data yet		
Sum:								





WP4 Result 4.10 Four specific trainings in the Green Economy



WP & Activity	Partner	Target group	No. of participants	Timeline	Implementation report	Evaluation data	Evaluation report	Comments
WP4 A11.2 Construction technician	PP23 LVT	pending	pending	Testing planned for 2023	pending Trying to find participants but no interest, solution will be found later	no evaluation data yet	By PP11 RSU Latest by 30.06.24	Result 4.6 Two trainings Vocational Master
WP4 A12.2 Service technician	PP14 WIFI	Open for several target groups	pending	pending	pending Additional data will be instered (number of participants etc)	Curriculum will be available in summer 2023 (to be answered by PP15 HS02)		
WP4 A12.4 Development and implementation of modular training customer service technician	PP2 HWKD with BSZ Zeuner vocational school							
Sum:								





- WP4 A12.5 - timelines needed from Wlfi.
- Italy –ALL TRAININGS - Starting in November/December 2023 – March 2024 / end june latest implementation report.
- Lithuania additional training – WP4. A20 – start in January/March 2024 - finish planned for May 2024





Questions regarding
WP4 Second center level "Continuing
vocational training" ?



20min.
coffee
break





TOP 6

**WP5 Third center
level "Higher
education"**



WP5 Results Overview



<u>Results</u>	<u>Status</u>	<u>Deadline</u>	<u>Comments</u>
5.1 Two Dual Bachelor Degree Programs & Dual Bachelor program "Sustainable Management of SMEs"	Done	30.06.23	
5.2 Four Green Economy study modules	Ongoing	30.06.24	
5.3 Innovation support and R&D projects for SMEs	Ongoing	31.07.24	
5.4 Train the Trainer Programme for university lecturers and consultants	Almost done	30.06.23	
5.5 Dual Bachelor "Entrepreneurship & Innovation in Green Economy"	Ongoing	30.06.24	
5.6 Dual Bachelor program "Logistics - Green Supply Chains"	Ongoing	30.06.24	
5.7 Dual Bachelor program "Service technician"	Ongoing	30.06.24	
5.8 Tutorial "Sustainable management Climate neutrality for companies"	Ongoing	30.06.24	



WP & Activity	Partner	Target group	No. of participants	Timeline	Implementation report	Evaluation data	Evaluation report	Comments
WP4 A11.2 Construction technician	PP23 LVT	pending	pending	Testing planned for 2023	pending	no evaluation data yet	By PP11 RSU Latest by 30.06.24	Result 4.6 Two trainings Vocational Master
WP4 A12.2 Service technician	PP14 WIFI	Open for several target groups	pending	pending	pending	Curriculum will be available in summer 2023 (to be answered by PP15 HS02)		
WP4 A12.4 Development and implementation of modular training customer service technician	PP2 HWKD with BSZ Zeuner vocational school							
Sum:								



- WP5 A8.1
- RSU – no update, rest is clear
- Wp5 A8.2
- Lit
- WP5 A4 – training D
- Slupsk – implementation report ready by June 2024
- Panevėžys – training is finished, implementation report is needed
- WP5 43 – Slupsk additional activity, March – June 2024, implementation report end of July 2024, topic is agricultural activity (green farmers and digitalization for farmers). Evaluation - Panevėžys college will discuss this later with Melanie-

- Confindustria and the Uni testing for all activities is clear – end of July as implementation reports.





WP5 A8 Study modules “Green Economy”



- Short update by:
- PP14 WIFI

A Management & Technologies of the Water and Wastewater Industry	B Waste Management & Technologies	C Management & technologies of the circular economy	D Management of sustainable economic activity
• ?	• PP9 PC with PP8 PCCIC - starting 01.02.22	• PP9 PC with PP8 PCCIC	• PP6 APS • PP9 PC - starting 01.02.22 • PP11 RSU

→ Curricula ready ([in Gdrive](#))





Questions regarding
WP5 Third center level "Higher
education" ?



RnD Projects -

Cove Lithuania – there will be 2 additional projects





Wrap-up and evaluation of the meeting



Evaluation of this project meeting



- Surveymonkey link:

<https://www.surveymonkey.com/r/3loe-szczecin>



Co-funded by the
Erasmus+ Programme
of the European Union



Any other
questions or
comments?
